



NYC Parks

Community Board 7 Capital Projects Status Report June 2021





NYC Parks

Captain John McKenna, IV Park

Vanderbilt St. bet. E. 4 St. and E. 5 St., CB 7, CD39

Funding

TOTAL: \$200K

- CM Lander (FY18)

(Transferred from Thomas Cuite)

Scope

- Install water service to the park

Status

- Engineering and contract procurement to be included by Citywide Services in the next available contract
- Project to start construction summer 2021 and be complete fall 2021





NYC Parks

Prospect Expressway Sitting Areas

Sherman St & Ocean Parkway Service Road, CB7, CD39

Funding

TOTAL - \$720K


- \$360k CM Lander (FY20)
- \$360k BP Adams (FY20)

Scope


Install tot play equipment on the Sherman Street site, new seating, fix water service, new landscaping

Status

- In Design, to be complete spring 2021
- Construction to start spring 2023 and be complete spring 2024
- Due to Covid-19 pandemic, construction start date may be subject to change

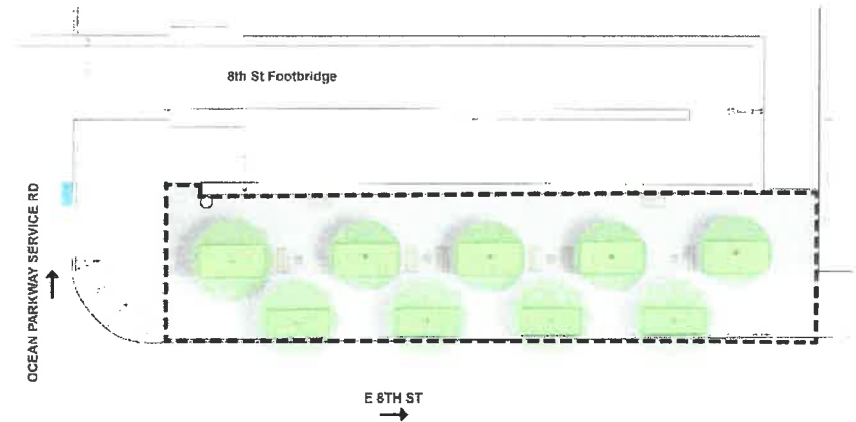

E 8th Street Seating Area | Schematic Design

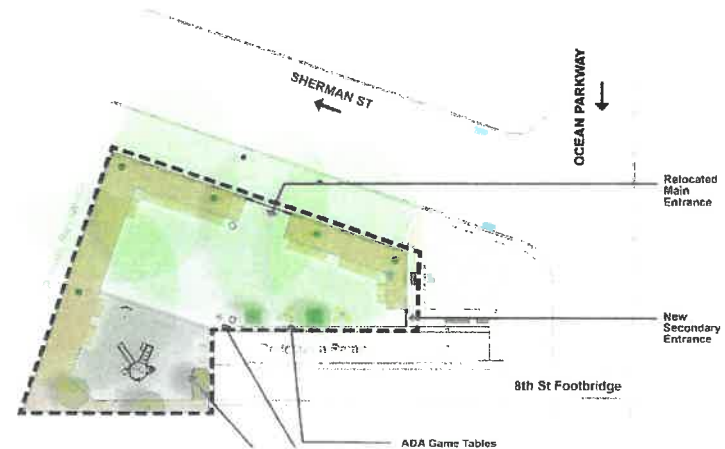



NYC Parks

Sunset Park (Phase 4) – Paving

41 St., 44 St., bet. 5 Ave. and 7 Ave., CB 7

Funding

TOTAL: \$600K


- CM Menchaca/BP Adams (FY17)
 - Participatory Budgeting

Scope

- Repaving paths and stairs in most needed locations

Status

- Scope meeting held October 11, 2016
- Design completed August 2018
- Construction started October 2019 and was completed fall 2020

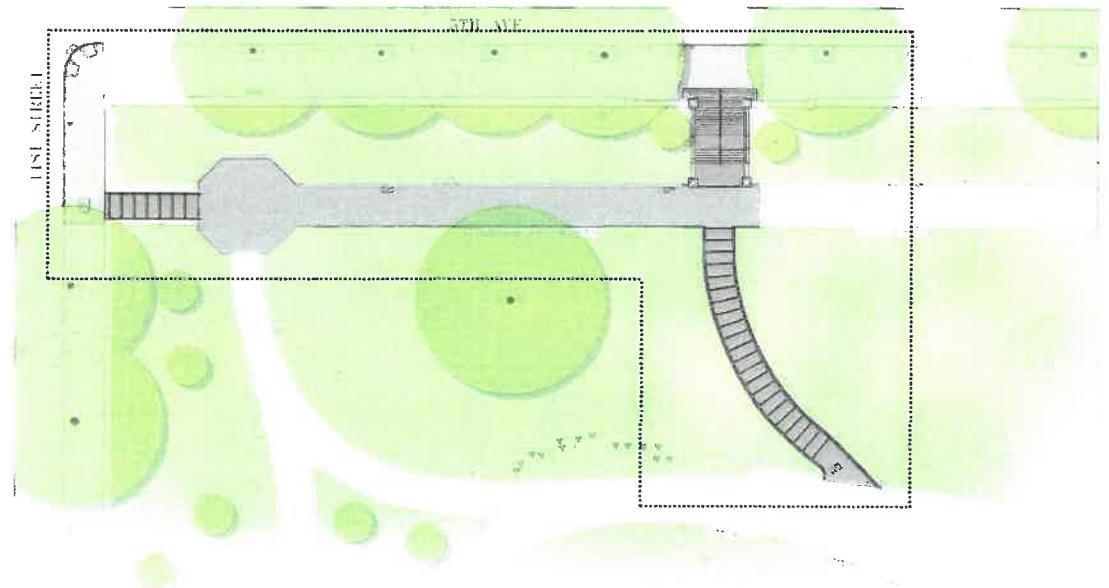

AREA OF RECONSTRUCTION:
• RECONSTRUCT CONCRETE SIDEWALK
• RECONSTRUCT GRANITE STAIRS
• RECONSTRUCT CONCRETE STAIRS
• RECONSTRUCT ASPHALT PATHWAY
• NEW DECORATIVE STEEL HANDRAILS

DRAFT



NYC Parks

Sunset Park (Phase 5) – Handball Courts

41 St., 44 St., bet. 5 Ave. and 7 Ave., CB 7, CD38

Funding

TOTAL: \$500K


- CM Menchaca
 - Participatory Budgeting

Scope

- Reconstruction of handball courts

Status

- Scope meeting held June 28th, 2018
- Design completed spring 2019
- Construction started spring 2021 and is estimated to be complete spring 2022

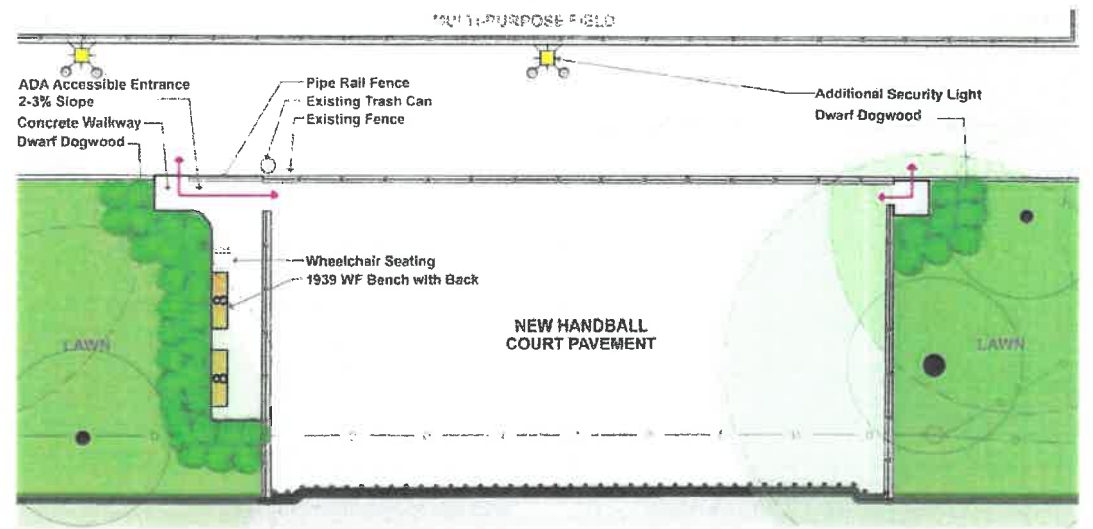



NYC Parks

Rainbow Playground

55th and 56th St. & 6th Ave., CB 7

Funding

Total: \$1.6M


- \$500K CM Menchaca (FY19)
- \$1.1M CM Menchaca (FY20)

Scope

- Complete reconstruction of playground including play equipment, safety surface, bollard spray shower, drainage, pavement, one full basketball court, color seal coat, lexan backboards with hoops and nets, benches, drinking fountains, and landscaping.

Status

- Scope meeting held on November 25th, 2019
- Design completed fall 2020
- Construction to start fall 2022 and be completed fall 2023
- Due to Covid-19 pandemic, construction start date may be subject to change

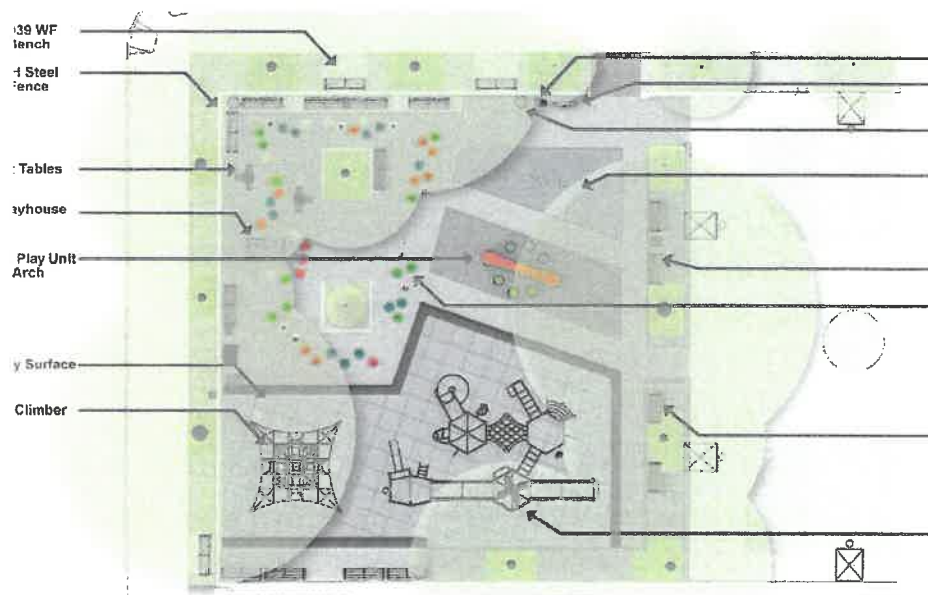



NYC Parks

Sunset Park: Recreation Center

44th St. & 7th Ave., CB 7, CD38

Funding

TOTAL: \$2.857M

- Mayoral

Scope

- Enclose the atrium space and address heating and cooling throughout the center.

Status

- Design completed fall 2017
- Construction start delayed, project was rebid
- Construction to start spring 2022 and be complete fall 2023
- Due to Covid-19 pandemic, construction start dates may be subject to change

